

## GDA CONSULTATIVE GROUP THURSDAY 22<sup>ND</sup> SEPTEMBER 2016



#### **OVERVIEW**



- HSE Projects
- DIT Projects
  - Programme 1
  - Programme 2
  - Programme 3
- Other Projects
- Grangegorman Employment Charter Compliance
- Labour and Learning Forum
- Public Art
- Communications/Community

#### **HSE PRIMARY CARE CENTRE**



Start Date: 13th April 2015 Completion

Date: By end of 2016

• Contractor: L & M Keating Ltd .

**Contract Value:** €7.5m + €1.2m

- **Programme**: Audiology suite revised works to interior are on programme.
- Brickwork is completed
- Audiology test pod rooms are in manufacture
   delivery from mid August.
- Landscape works commenced on site.
- Most site services are complete.
- HSE's Furniture fit out and occupation plan process is beginning.

#### **Employment**

Overall: 47 persons weekly average



## **COMMUNITY NURSING UNIT**




#### **Timeline**

- Shortlist & Issue of ITT Invitation to Tender Nov 2016
- Appointment of design team


Mar 2017


Stage 1 Design Report
 June 2017

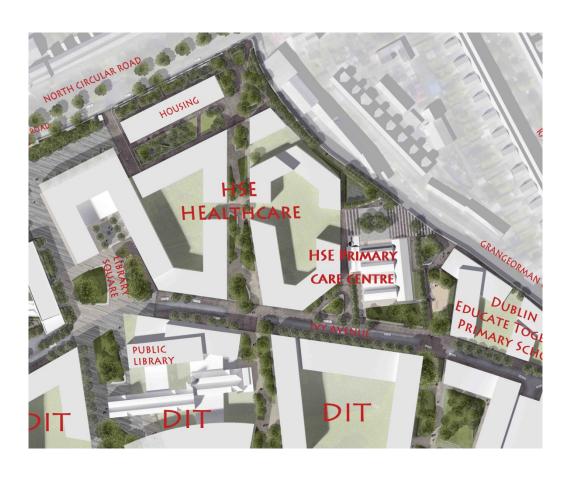

## NCR Car Park – Options



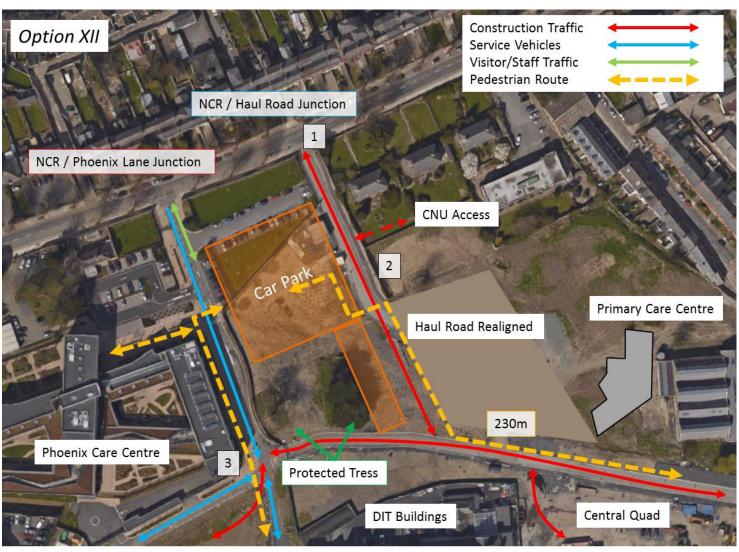

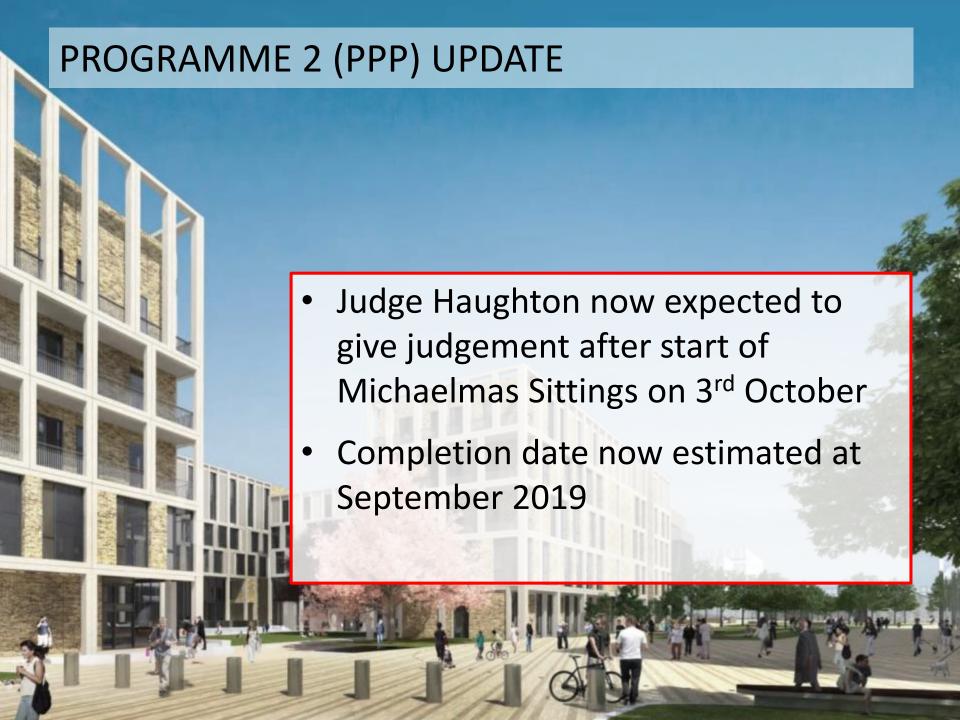

#### **BROADSTONE GATE – UNDER CONSTRUCTION**

- Currently excavating and removing material to create Broadstone plaza
- New bridge over the Luas tracks operational









#### **BROADSTONE GATE – UNDER CONSTRUCTION**

- Luas tracks installed across
   Constitution Hill
- Public & Bus Access road constructed and operational
- Archaeology on-going
- Commenced removal of perimeter wall with GG










#### **DIT PROGRAMME 3 PROGRESS REPORT**



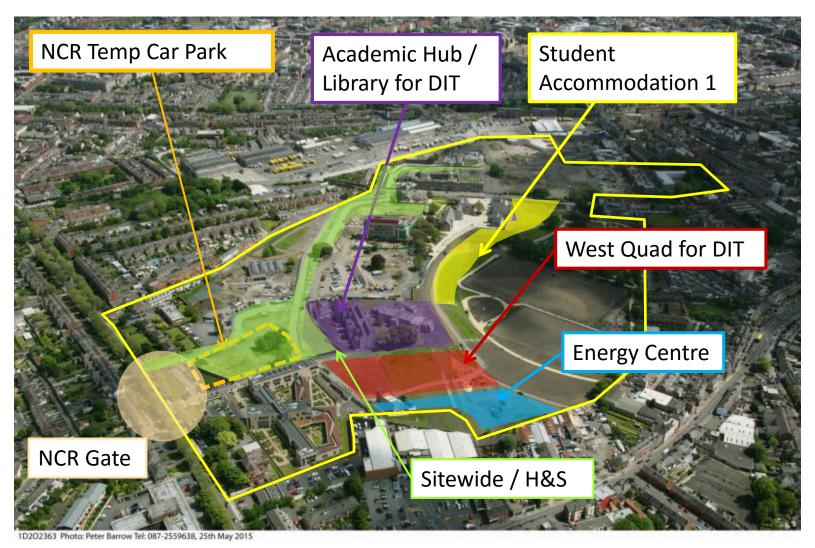

#### **DIT PROGRAMME 3 PROGRESS**



## **Energy Centre**

GDA to meet DoES shortly

to review project



#### **PROGRAMME 3 PROGRESS**


#### Grangegorman Development Agency Ghlomisireacht Foctsortha Ghráinseach Ghormáin

#### **Academic Hub**

 O' Donnell + Tuomey are working on initial design

#### **Target Dates**

- Planning Submission Jan 2017
- Planning Approval circa –March 2017
- Detail Design Jan 2017
- Tender (contractor) Nov2017
- Start on Site Jan 2018
- Handover to DIT June 2019
- Occupation September 2019

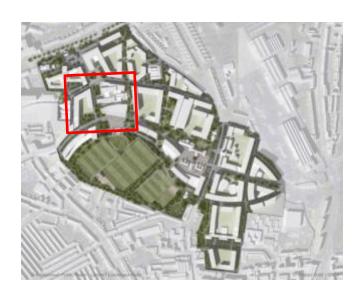



### **STUDENT ACCOMMODATION – UPDATE**




Procurement process ongoing



#### PRIMARY SCHOOL D7ETNS

- Planning Scheme Amendment16 to 24 classrooms
- Validation report on demographics issued
- GDA briefing of Local Area
   Committee undertaken
- Propose to engage in formal SDZ amendment process asap
- Traffic management study by Aecom in support of Grangegorman Upper Part VIII

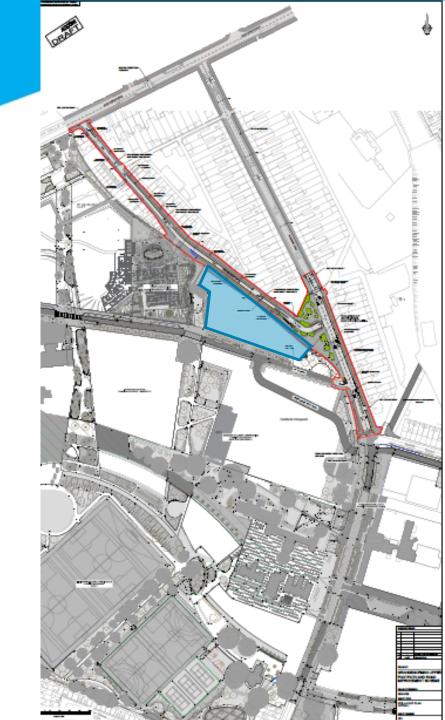

# UPDATE ON GRANGEGORMAN NEIGHBOURING SITES







#### **GRANGEGORMAN EMPLOYMENT CHARTER COMPLIANCE**


**GRANGEGORMAN EMPLOYMENT CHARTER COMPLIANCE** 


**Month Ending:** 

June 2016

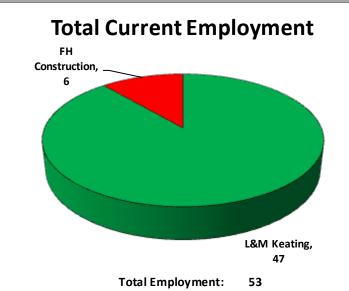

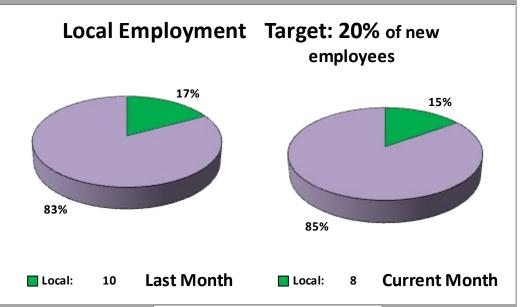





# GRANGEGORMAN LABOUR AND LEARNING FORUM





















## **GRANGEGORMAN PUBLIC ART**


















## **COMMUNICATIONS/COMMUNITY**



## **Ongoing Communications**

- Summer newsletter delivered
  - 100 provided to Constitution Hill flats
- Ongoing support for Public Art Programme
  - Admin support for Pathway 6 Lending for Primary Care Centre
- End of Year Report 2015 now complete and available on GDA website





## **COMMUNICATIONS/COMMUNITY**



#### Meetings

- Community Liaison Committee meeting took place on 20<sup>th</sup> July
  - Terry Prendergast attended to discuss Student Housing in area
  - Request made that security audit of site is carried out
  - Complaint made about sporadic attendance at meetings. To be discussed at next meeting
- Meeting with Central Area Councillors on Dublin 7
   Educate Together
  - Support for process based on RPS report
  - Believe a public meeting called by Councillors may be necessary

## **Pitches**





- The Grass pitches are now open
- All bookings organised through DIT Sports

## **THANK YOU**



