## **Grangegorman Consultative Group 12<sup>th</sup> September 2013**

## Grangegorman Development Agency Gníomhaireacht Forbartha Ghráinseach Ghormáin

#### **PROJECT UPDATE**

Ger Casey
Grangegorman Development Agency




## Programme 1 (2012-2014)



### Strategy:

- ~8,000m² of existing protected structures brought back into use for educational purposes
- Consolidates Art, Design, Photography & Social
   Science
- New build 4,500m2 research / incubation (PRTLI)
- Over 1,000 students and staff on site by 2014

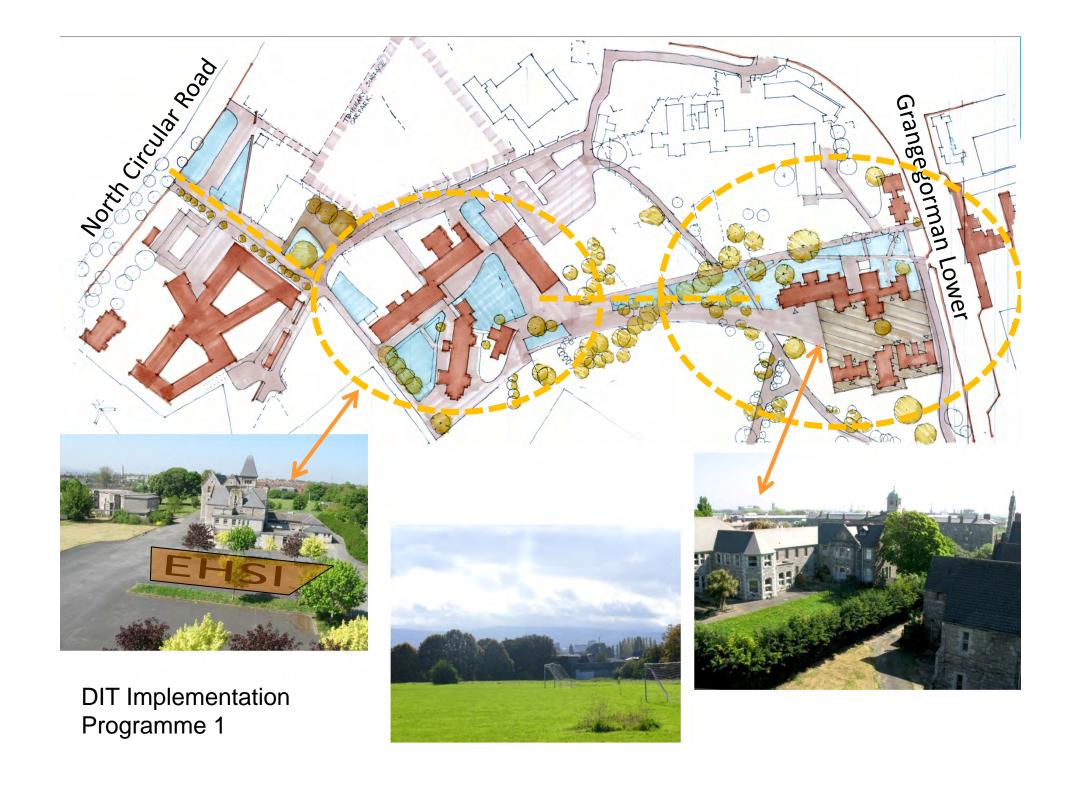

## CONSERVATION AND STABILISATION WORKS



- Consultants Coady, DBFL, DLPKS
- DCC has approved Section 5 works for the Top House.
- Asbestos Surveys complete
- Immediate Stabilisation Works (Top House) completed

#### **SECONDARY PHASE WORKS – 1/2**

### Top House (08)

- Minimum Stabilisation

### **Roman Catholic Chapel (21)**

- Minimal / finished works

#### **Church of Ireland Chapel (24)**

- Mothballing

### **Clock Tower (28)**


- Minimal / finished + mothballing

#### Lower House (32)

- Mothballing













#### SECONDARY PHASE WORKS – 2/2

#### **Other Structures by Adaptive Reuse Team:**

Mortuary (17)



Grangegorman Development Agency



Gateway (18)

Female House (19)



Male Infirmary (20)

Female Infirmary (22)





**Tunnel** 

## **Adaptive Re-use**



- Consultants Taylor/ JJ O'Connell/ ARUP/ Ethos/ DLPKS
- Status Tender, Report for structure 8 and 9 due
- Planning Permission Date 15<sup>th</sup> March, 2013
- **Target Tender Date** September 2013
- Contractors Appointment Date October 2013
- Works Completion Date August 2014



### **Environmental Health Sciences Institute**



- Consultants RKD, ARUP, Bruce Shaw, Sweet
- Status Tender Pre-qualification
- Planning Application 10<sup>th</sup> December 2012, revised planning notification to grant – 12<sup>th</sup> August, 2013
- Target Tender Date Oct 2013
- Contractor Appointment Date Feb 2014
- Works Completion Date August 2015

## **EHSI**











### **DEMOLITIONS**



- Consultants Coady, DBFL, DLPKS
- Status Onsite
- Planning Application on 9<sup>th</sup> October 2012
  - Permission 3rd December 2013
- Target Tender Date 18<sup>th</sup> February 2013
- Contractor Appointment Date April 2013
- Works Completion Date End Oct 2013

## **Demolitions**

The Nurses Home







## **Demolitions**









## **Archaeology**

#### **Old Basements**










## SITE INFRASTRUCTURE / PUBLIC REALM



- Consultants MRY/ DMOD/ ARUP/ Lutzow 7
- Status Tender
- Planning Application on 18<sup>th</sup> October 2012
  - Planning Permission 12<sup>th</sup> December 2012
- Target Tender Date April 2013
- Contractor Appointment Date July 2013
- Works Completion Date September 2014

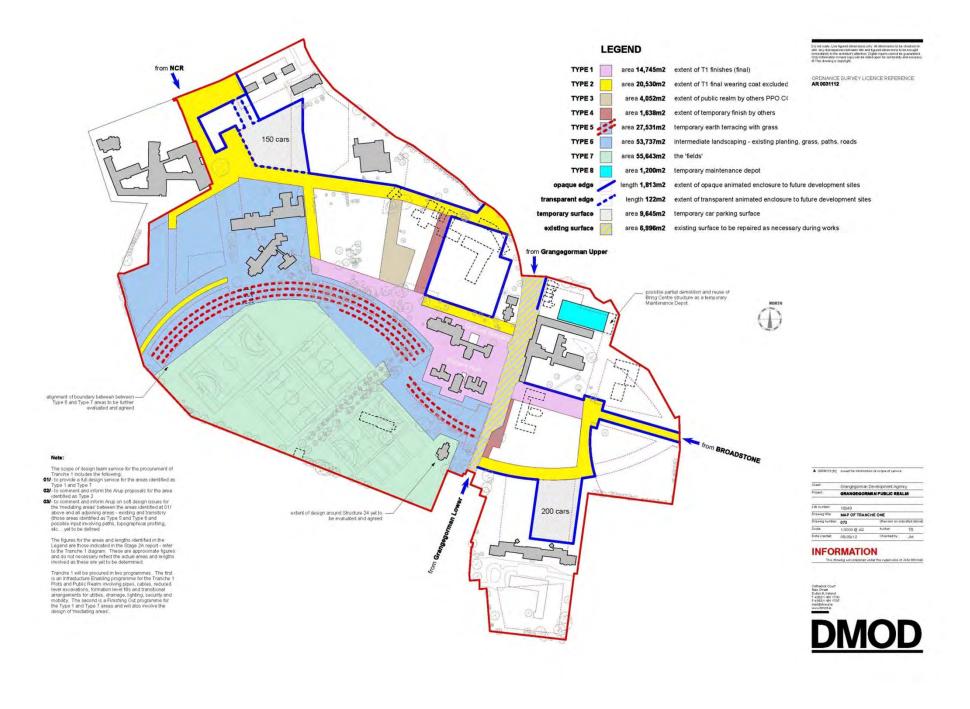

# **CENTRAL & EAST QUAD PPP'S**



- Outline Briefs completed
- NDFA/GDA/DIT collaboration
- TA appointed Dec 2012
- Business case completed
- EIB Support Regeneration,
   Education, Research, Technology
   transfer
- OJEU September 2013
- Marketing Day took place
- On programme



## CENTRAL & EAST QUAD PPP MARKETING DAY



- Launched by the Minister for Education and Skills
- Over 120 attendees from around 40 companies
- A lot of interest and enthusiasm shown for the project












### **Other DIT Developments**



- Provision of infrastructure will allow self funding elements to progress:
- Student Accommodation:
  - Immediate opportunity for ~600 beds/ 20,000m² / €70M
  - Capacity on site for 1,600 beds
- Sports facilities student levy and sinking fund in place
- Science Park with third parties
- Commercial outlets- shops etc

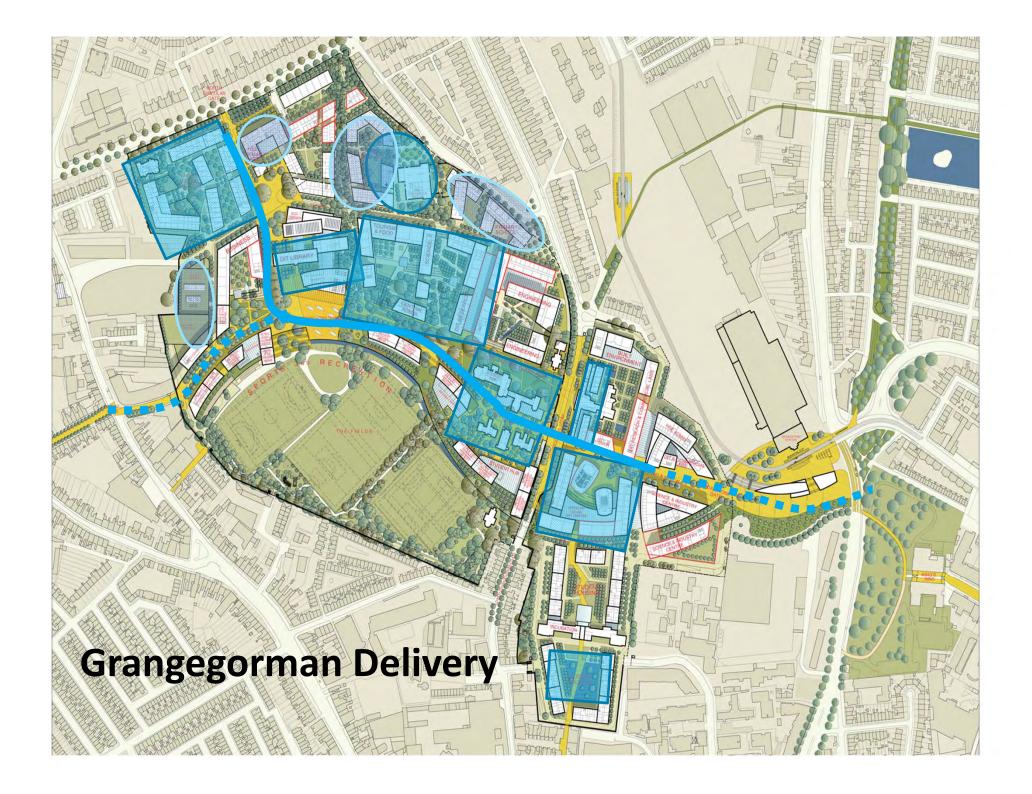

## **THANK YOU**



