

CONSULTATIVE GROUP – 19 MARCH 2015

Michael G Hand Chief Executive Officer Grangegorman Development Agency



OVERVIEW



- Planning
- HSE Projects
 - Phoenix Care Centre
 - Primary Care Centre
 - Community Nursing Unit
- DIT Projects
 - Site Infrastructure / Public Realm
 - DIT Research Hub
 - Public Private Partnerships (PPP's)
 - Replacement Bus Park Structure
 - Stabilisation of Lower House and Church of Ireland
 - Student Accommodation
 - D7ET National School
- Grangegorman Employment Charter Compliance
- Communications/Community

PLANNING APPLICATIONS

Clock Tower Disability access and misc. works Adaptive Reuse 'Wrap up' application-misc. works Bus Park Use of undercroft as carpark for Dublin Bus SIPR Ball catch netting to pitches Permission granted 10.02.15 Lodged 27.01.15 Lodged 13.03.15	Development	Proposed Works	Status	
Bus Park Use of undercroft as carpark for Dublin Bus SIPR Ball catch netting to 10.02.15 Lodged 27.01.15 Lodged 13.03.15	Clock Tower		_	
carpark for Dublin Bus SIPR Ball catch netting to Lodged 13.03.15	Adaptive Reuse	application-	_	
	Bus Park	carpark for Dublin	Lodged 27.01.15	
	SIPR		Lodged 13.03.15	

PHOENIX CARE CENTRE



- Defects period extended to 30th June 2015 by the Employer's Representative
- AECOM have notified GDA that Sisk will agree to carry out refurbishment of main high-trafficked doors (70 No). Method of work will be focused around safety and welfare of patients and staff
- Possible manufacturing defect with a number of locks is being investigated

PRIMARY CARE CENTRE

- Letter of Intent issued to L & M Keating Ltd on 19th February
- Works shall begin in March.
 Public Information Evening with the contractor to take place beforehand
- Programme of construction work is 60 weeks. HSE fitout to commence afterwards





COMMUNITY NURSING UNIT



- Scope of Feasibility Study extended to include alternative option for incorporation of St Elizabeth's Court Site into plot
- Draft Feasibility Study Report received and GDA comments to be incorporated prior to circulation of report

SI&PR



Programme/Progress

Overall programme is 94% complete

Employment

- Overall: 54 Persons Local: 20 Persons
- 37 % of local employees to all employees on site

SI&PR


- District heating welding and commissioning at east GG
- Site Clearance to rear gardens of HSE houses on GG Lower
- Landscaping and tree planting around the grass pitches
- Sports lighting and CCTV
- Bradogue culvert and trunk watermain









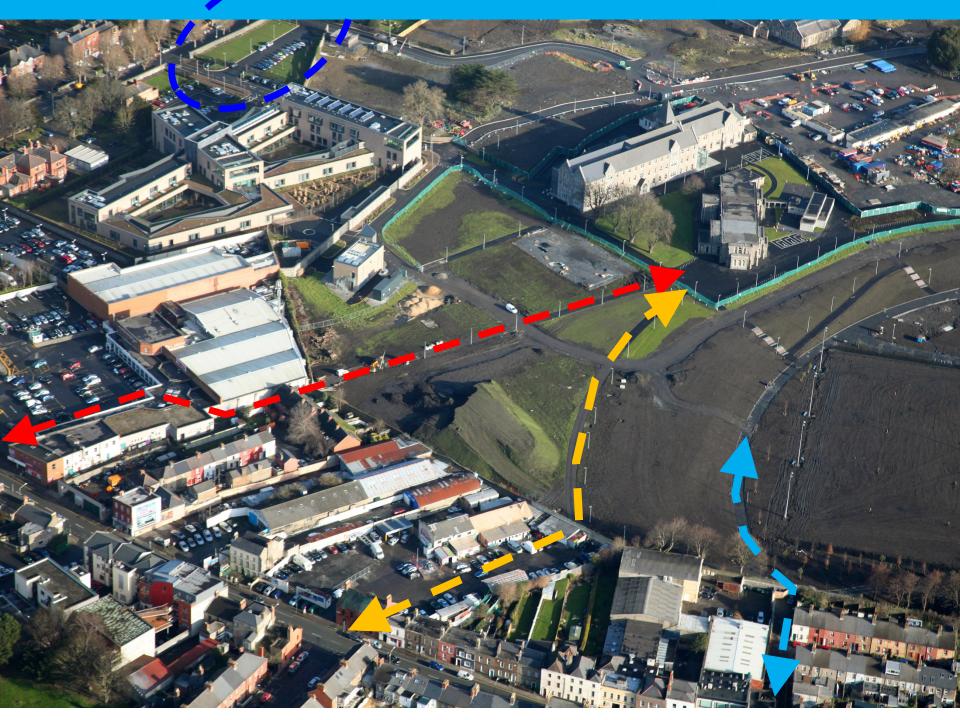

PARK SHOPPING CENTRE LINK



- Park SC commenced own works on 20th January 2015. Works almost complete
- Roadbridge have formed opening to perimeter wall. Completion of surface to pathway to be done in conjunction with landscaping of adjacent areas
- Date for target opening under review.





IVY AVENUE UTILITY SERVICES 100mm & Public Lighting Ducks 100mm & Security & Wireless Ducis 225mm & Storm Water 315mm & Tom Bar Gas Main 450mm & Occ Trunk Mains Water 200mm & Distribution Mains Water 150mm & MV Ducks 150mm & LV Ducas 24th ICT Network Duds 100mm & Communications Telco Ducis 100mm & Security & Wrekss Ducis 200mm & District Healing 100mm @ Public Lighting Ducks 300mm of Four Sower

SANTRY GATES REINSTALLED



- Before Repair works
- First erected at Grangegorman in 1940 from Santry House



SANTRY GATES REINSTALLED









SANTRY GATES REINSTALLED



Repair works carried out by Bushy Park Ironworks

Reinstalled on site 17th February 2015



THE GREENWAY HUB (EHSI & HHI)

Contractor – BAM Building

Programme

- BAM Target Completion Oct 2015
- Contract Completion December 2015
- On programme (50% complete)
- Plant Room Steel Roof completed
- External façade ongoing

Health & Safety

No reportable accidents on site

Employment

Overall: 55 persons

Local: 5 persons





THE GREENWAY HUB - INTERNAL











THE GREENWAY HUB - EXTERNAL














THE GREENWAY HUB (EHSI & HHI)

- Topping off Ceremony for the Research Hub took place Friday 13th March
- Minister Bruton, Minister for Jobs, Enterprise and Innovation laid the final brick on the roof of the building.








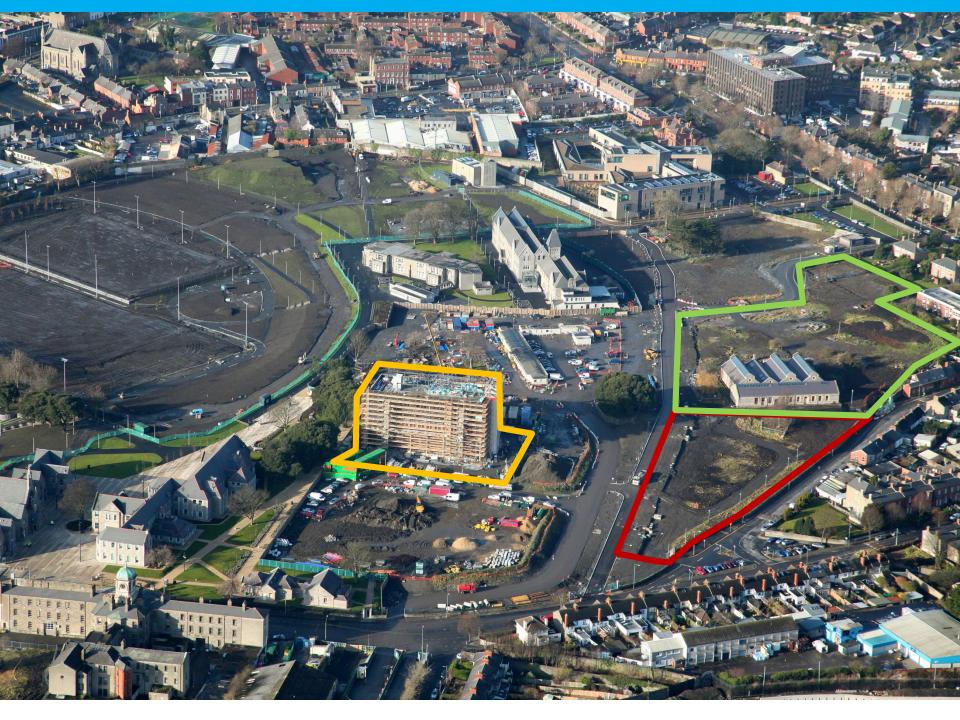

PROGRAMME 2 PPP TENDERING PROCESS

- 2012 Sept Dec
 - Appoint technical advisors
 - Fixtures, fittings and equip
- 2013 Jan August
 - Outline design
 - PPP Operational specs
- 2013 Aug- Oct 2015
 - PPP tender 28th Nov 14
 - Preferred bidder Feb 15
 - Financial close Oct 15
- 2015-2017
 - Construction
- September 2017
 - 10,000 students on campus

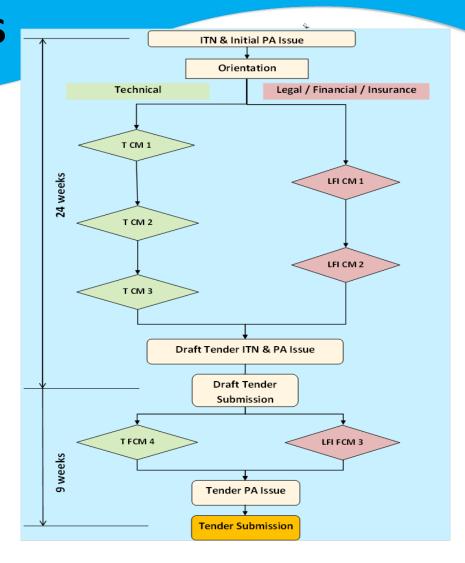

Process on schedule – significant on-going interaction with NDFA & DoES



REPLACEMENT BUS PARK STRUCTURE



Programme/Progress


- Overall 95% complete
- Bus Park operational in April 2015

Employment

Overall: 15 Persons

Local: 1 Person

 7% of local employees to all employees on site

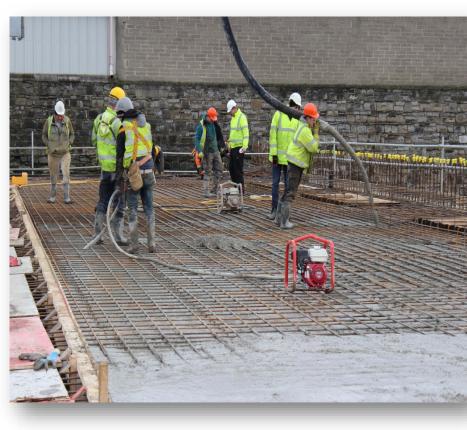

REPLACEMENT BUS PARK STRUCTURE

Grangegorman
Development Agency
Gníomhaireacht Forbartha
Ghráinseach Ghormáin

- Commencement of:
 - electrical works
 - repair works to limestone wall
- Preparation works for:
 - pouring concrete screed and stairs
 - slab tie-in detail on top of wall
- Protection and diversion of existing services at Broadstone





STABILISATION & CONSERVATION

Lower House & Church of Ireland

Programme

- Commencement on site
- Substantial Completion target date

25 November 2014

29 May 2015

Progress

- programme of stone repair, lime mortar and stone capping and repointing on the southern façade
- Areas of significant heritage value have been located within the Central Block of the Lower House
- Proposals to re-roof part of the building have been submitted by the Design Team, CPA
- Works to the Church of Ireland progressing well and the new areas of slate roof are now 60% complete


Employment

• Overall: 22 Persons Local: 8 Persons

STUDENT ACCOMMODATION



- Phase 1 is comprised of three blocks in the centre of the west campus.
- It will provide accommodation for up to 700 students.
- This is in pre-procurement process with the expectation to issue the tender for construction in early 2016.

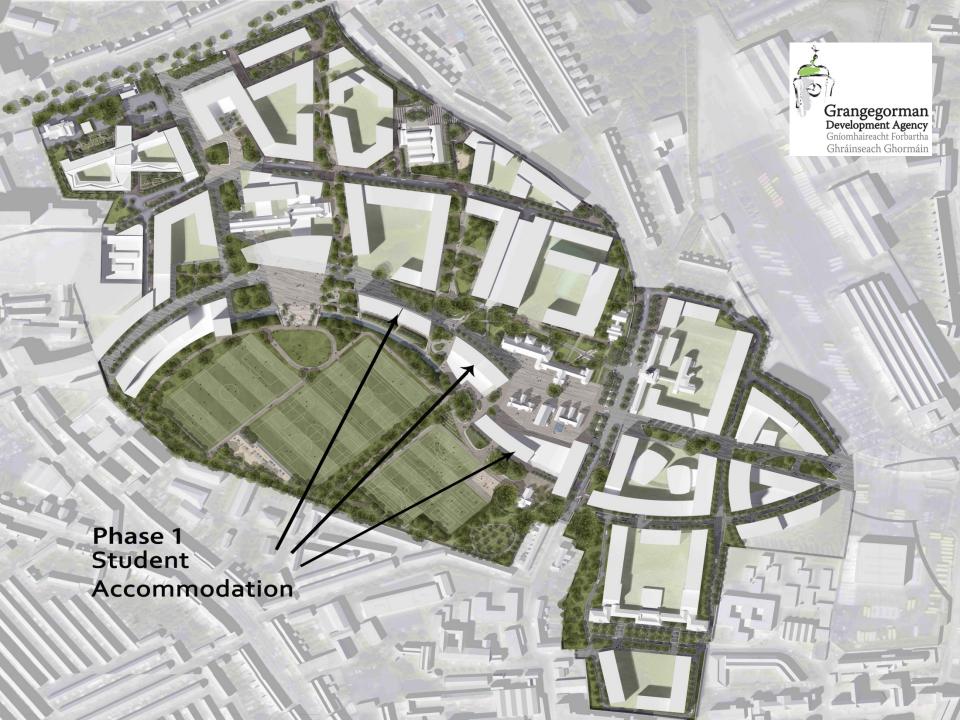

DUBLIN 7 – NATIONAL SCHOOL




- Expressions of Interest (EOI) for Single Party Framework for Architectural Led Design Team Services returned on 2nd February
- Shortlisting to 5 Teams complete.
 Tender Documents to be issued in coming weeks
- SDZ Planning Scheme Amendment required for 24 classrooms





GRANGEGORMAN EMPLOYMENT CHARTER COMPLIANCE


GRANGEGORMAN EMPLOYMENT CHARTER COMPLIANCE


Month Ending: January2015

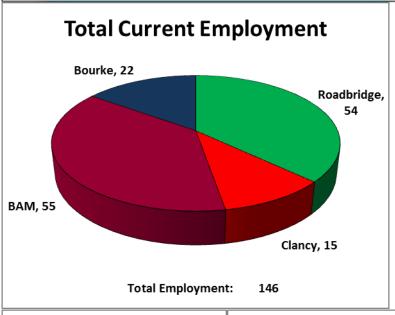


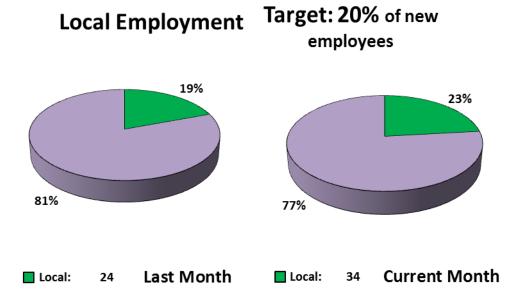









LABOUR AND LEARNING FORUM



Skills Register

In conjunction with LES updating database of CV's for contractors

Business Event

 An event for local business with Dublin Chamber on March 24th at 5.30pm

ABC Child Poverty Project

- Finalising Consortium Agreement with Pobal
- Advertisement for Coordinator and Administrator
- Intervention Project Commence August 2015

COMMUNICATIONS/COMMUNITY

GDA Elections

- Election Process for Community representatives to the GDA Board and Consultative Group has started
- List of registered Groups to be published shortly
- Election date set for 30th April 2015

General Communication

- Public Information Evening for ongoing and upcoming works to the HSE Quarter and North of Ivy Avenue took place
 28th January
- GG Gates reinstalled in place with great community feedback on social media

Public Art Working Group

- Deadline for submissions for role of Public Art Coordinator 23rd
 March
- Tenders will be evaluated before the next PAWG meeting in April





COMMUNICATIONS/COMMUNITY



- Community Liaison Committee (CLC) Meeting took place 18th February
 - Issue of use of area behind GG Villas East as Workers Compound
 - Issue regarding alleged damage to houses due to construction works
 - Breach of Working Hours
 - SIPR works and planting to back of GG Villas East discussed

General Community Queries

Issues raised through the last Public Information Evening, GDA attendance at a Residents Association meeting and general queries include:

- Parking onsite and along GG road
- Traffic Management
- Road repair at GG road site construction crossing
- Use of Ivy Avenue
- Opening of the playground and pitches for community use

THANK YOU



